

LAND ACKNOWLEDGEMENT

MetroLinx acknowledges that we connect communities by building and operating transit within the traditional lands of the Anishinaabe, the Haudenosaunee and the Wendat peoples, for whom these lands continue to have great importance.

Treaties between First Nations and governments cover these lands, and the promises contained in these Treaties remain relevant to this day.

MetroLinx and its employees are committed to understanding the history of these lands and the continued impacts of colonization and take responsibility for actions to advance reconciliation.

MetroLinx will continue to seek the knowledge, expertise and experience of Indigenous partners and commits to doing business in a manner that is built on a foundation of trust, respect, and collaboration.



AGENDA

1. Welcome (5 minutes)


- Land Acknowledgement
- Safety moment
- CLC overview & introductions

2. Construction updates (25 Minutes)

- Temporary Bus Loop
- Elevated Guideway
- Don Valley Station
- Flemingdon Park Station
- Current work
- Upcoming work
- Construction look-ahead

3. Community-led discussion (25 Minutes)

4. Next steps (5 Minutes)

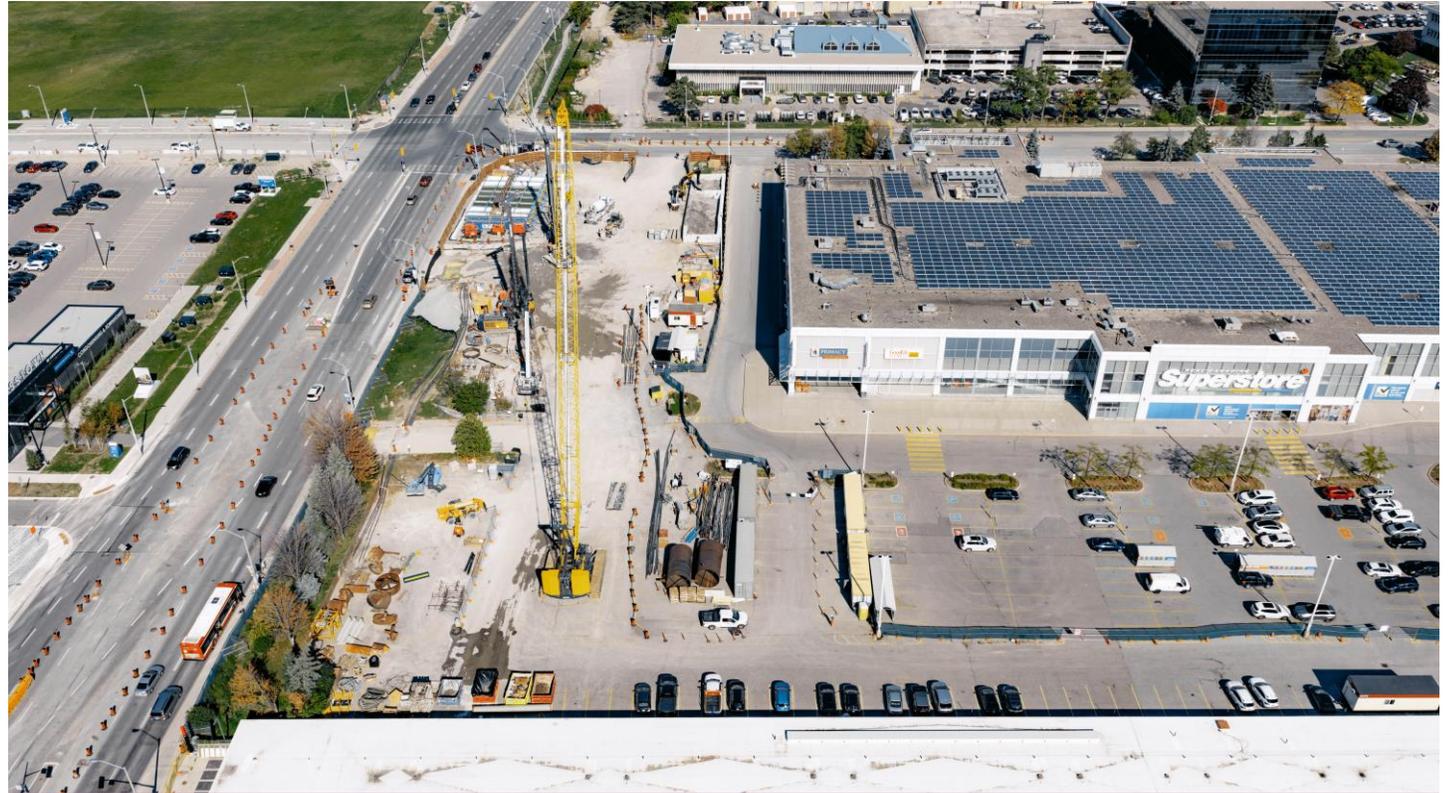

Guideway construction site - looking north just east of Don Mills Road

Safety Moment: Safety signage near a construction sites

Here are some reminders of the importance of safety signage near construction sites:

Preventing Accidents

- Signs are used to solicit the attention of motorists and pedestrians to potential hazards to reduce harm or injury.

Protecting the public

- Clear and visible signage informs and assist motorists and pedestrians to navigate construction zones safely.

Regulatory Compliance

- Health and Safety regulations require specific signage to be posted in visible locations.

Communicating hazards

- Signage often restricts access to construction zones to reduce exposure to potential hazardous incidents.

Culture of Safety

- Reinforce the importance of safety rules and that it everyone's responsibility to maintain a safe environment.



Don Mills Road south of Eglinton Ave. E.

Construction update: temporary bus loop

Temporary bus loop at Line 5 Don Valley Station

Construction ongoing until late October 2025

Completed work:

- Curb and platform
- Paving of bus loop
- TTC bus test completion
- Installation of temporary lighting
- CCTV installation
- Testing and commissioning of traffic lights and signals

Ongoing work:

- Testing and commissioning of lighting systems and CCTV systems is underway.

Upcoming work:

- Wayfinding signage is in production.
- Preventative maintenance.



Temporary bus loop construction - west



Temporary bus loop construction - east


Construction Update: Don Valley Station and Elevated Guideway

EIGHT WEEK LOOK-AHEAD: October 8 - December 3, 2025


#	Activity	Location	Start date	Duration	Impact	Hours of Work	Mitigations
1.	Piling drilling Building pier foundations for the elevated guideway	East side of Don Mills Rd. between Eglinton Ave. and Mike Palmateer Rd.	Ongoing	Four months	Dust and noise	Weekdays from 7 a.m. - 5 p.m. with periodic evening and weekend work	Solid hoarding, water misting, street sweeping, dust screens, limiting overnight work
2.	Watermain relocation	Don Mills Rd. between Eglinton Ave. and Gateway Blvd.	Phase 12: Oct. 14 Phase 13: Oct. 21	Phase 12: One week Phase 13: One month	Temporary traffic and TTC impacts, minor noise and dust	Weekdays from 7 a.m. to 5 p.m.	Dust screens, street sweeping, and advance traffic signage
3.	Trenching work Connecting the water and slurry pipe	Wynford Dr. and Don Mills Rd.	Starting Oct. 14	Five days (3 days of overnight work)	Noise, dust, and vibration	Daytime and overnight	Solid noise barriers, water misting, limiting roller usage during compaction work
4.	Site preparation Preparing the site for pile drilling (install site fencing and mobilize equipment)	Don Mills Rd. and Eglinton Ave. (825 Don Mills Rd.)	Starting mid-October	Three months	Pedestrian diversions, tree removals, clearing and grubbing	Weekdays during the daytime	Solid hoarding, traffic control measures, tree protection, noise, vibration, and air quality monitoring

Upcoming Traffic Configuration: Watermain Relocation Phases 12 and 13

Phase 12:
Starting
October 14,
2025, and
ongoing until
October 21,
2024

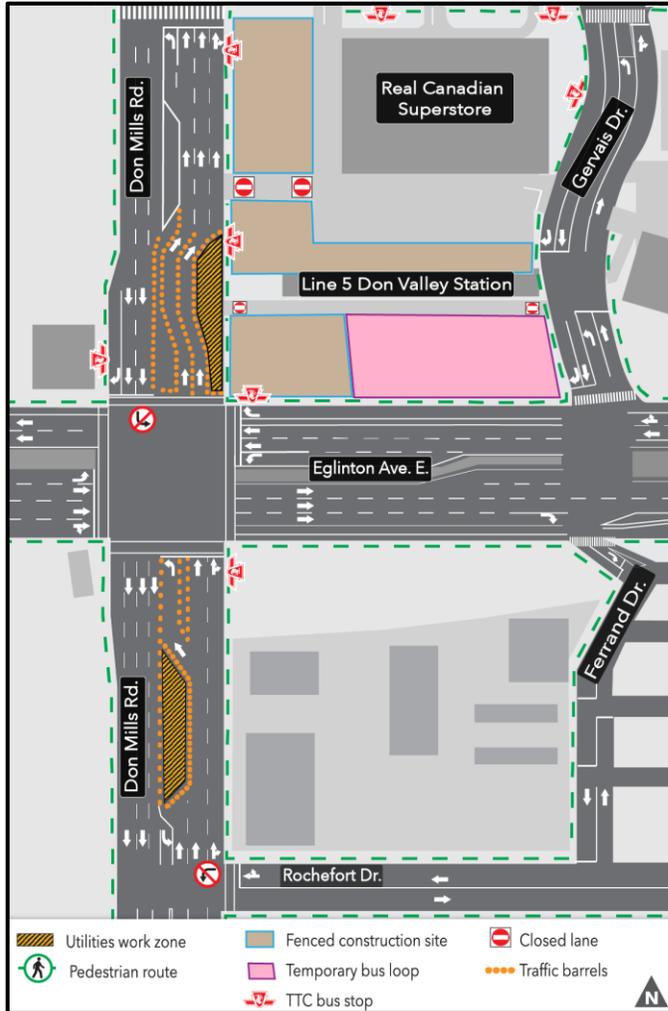

Phase 13:
Starting
October 21,
2025, and
ongoing until
November 18,
2025

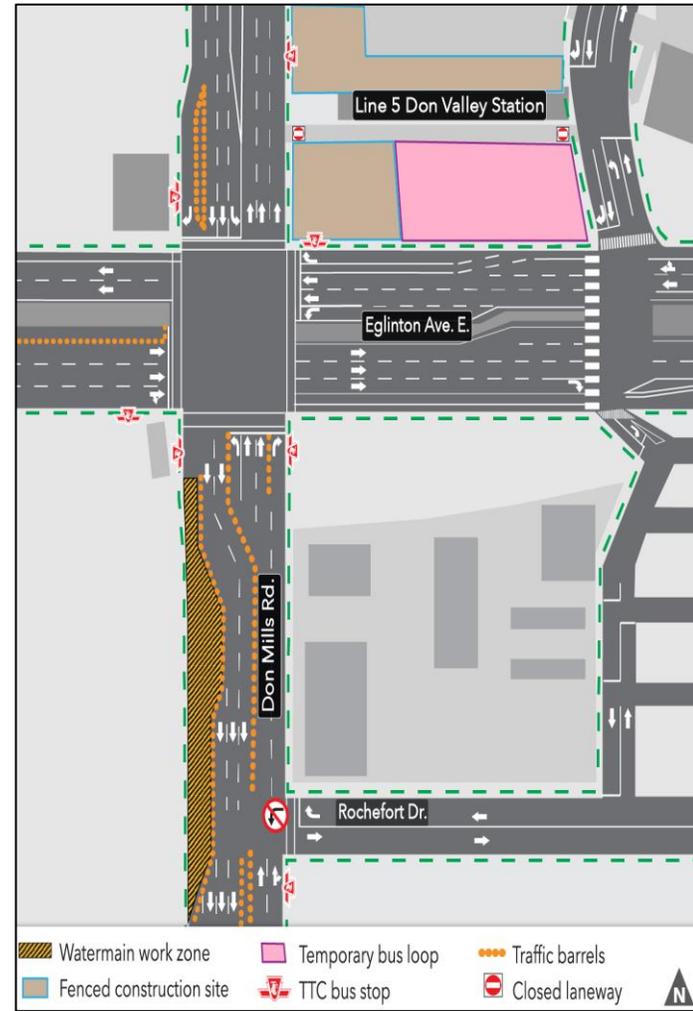



Overnight Trenching work at Wynford Drive

Start date and work hours:

- Starting October 14, 2025, for five days
- This work is expected to take five (5) days to complete between 7 a.m. to 7 p.m. and 9 p.m. to 5 a.m.


Traffic and pedestrian impacts:

- For night work on days 1 - 3, crews will close half of Wynford Drive between Don Mills Road and the entrance lane to St. Andrew Kim Catholic Church.
- **For night work on days 4 - 5, crews will close Wynford Drive completely, between the hours of 1:30 a.m. and 5 a.m. to install and connect the water and slurry pipes.**
- Pedestrian sidewalk will be temporarily closed near the work zone.
- Advance signage and flagger will direct pedestrians to use the adjacent sidewalk.
- No TTC bus impacts are expected.

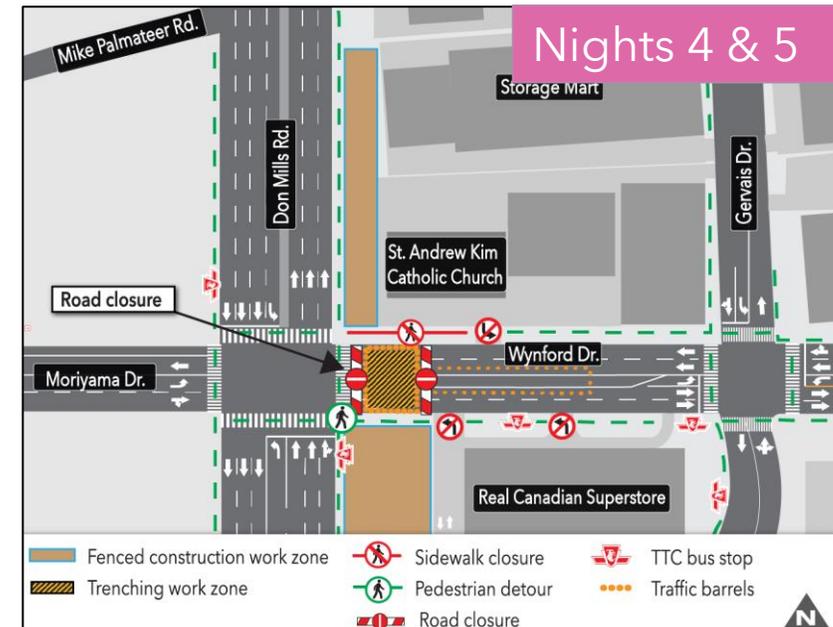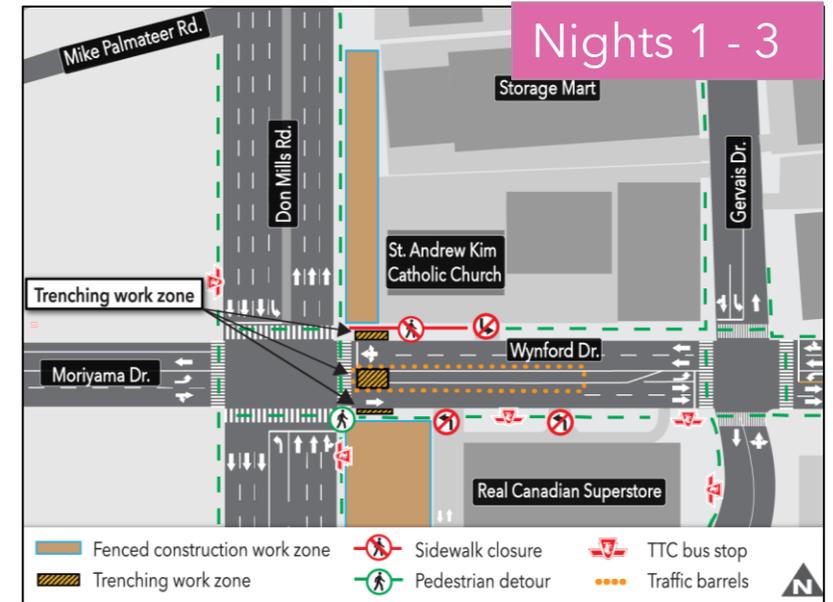

Elevated Guideway Construction: Piling Update

Pile No.	Timeline	Status
D-39	Started Sept. 8 and completed on Sept. 26	<ul style="list-style-type: none"> ✓ Drilling finished Sept. 18 ✓ Concrete finished Sept. 19
D-40 and D-41	Ongoing until late October 2025	<ul style="list-style-type: none"> • Drilling is ongoing
D-38 and D-37	Starting in late October 2025 until late November 2025	Not started
D-42 and D-43	Starting in late November 2025 until December 2025	Not started
D-36	January 2026 until February 2026	Not started

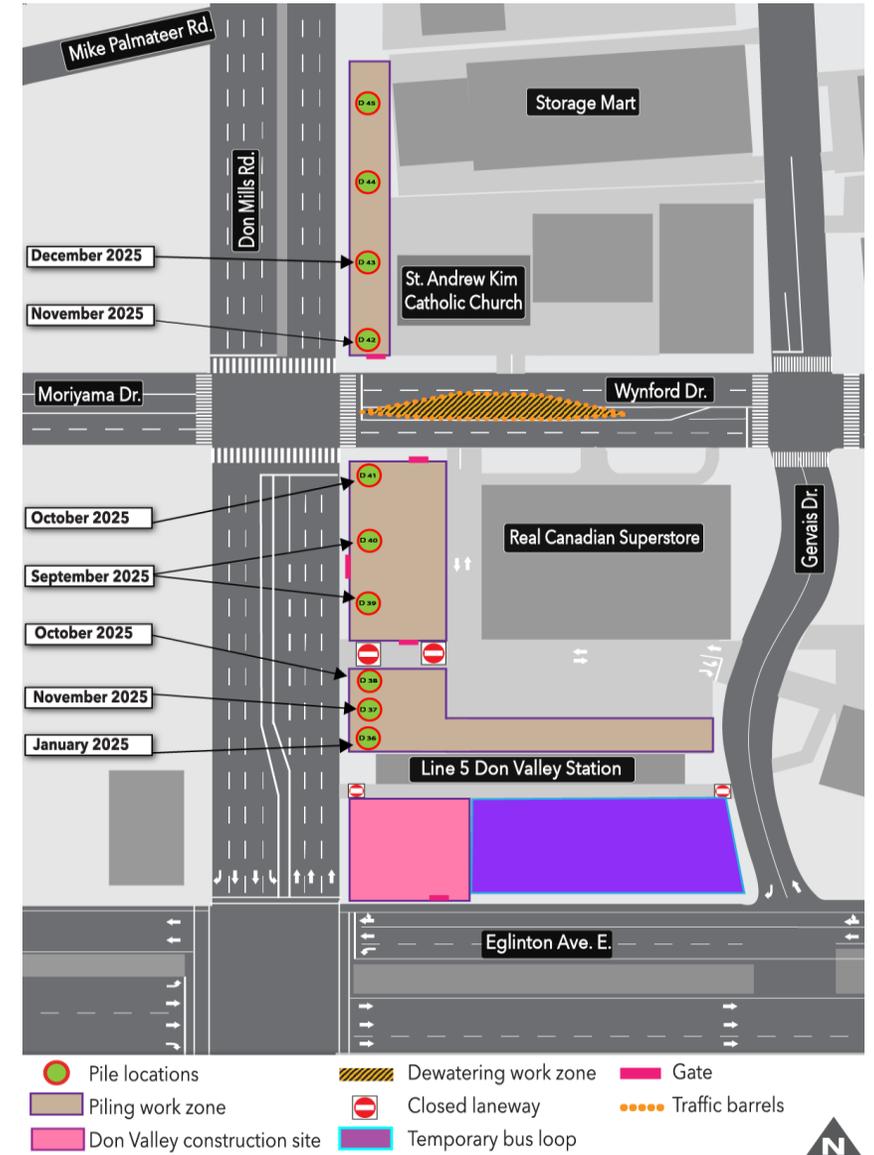

Upcoming Traffic Configuration: Don Valley Station Construction

Start date and work hours:


- Starting early November and into 2026
- Work in the Don Valley Station site is expected to take place on weekdays between 7 a.m. - 5 p.m.
- Overnight and weekend work may be required and will be communicated in advance

Work activities:

- Installation of site fencing, gates, and solid hoarding
- Tree protection and removal, clearing and grubbing
- Mobilization of piling equipment, rig and set-up for drilling

Traffic and pedestrian impacts:

- A temporary pedestrian walkway will be installed at the north-east corner of Don Mills Rd. and Eglinton Ave. E.
- Closure of the westbound curb lane on Eglinton Ave. east of Don Mills Rd., and the northbound curb lane on Don Mills Rd. north of Eglinton Ave. E.
- TTC bus stop #2263 will be relocated to north-west corner of Eglinton Ave. E. and Don Mills Rd.

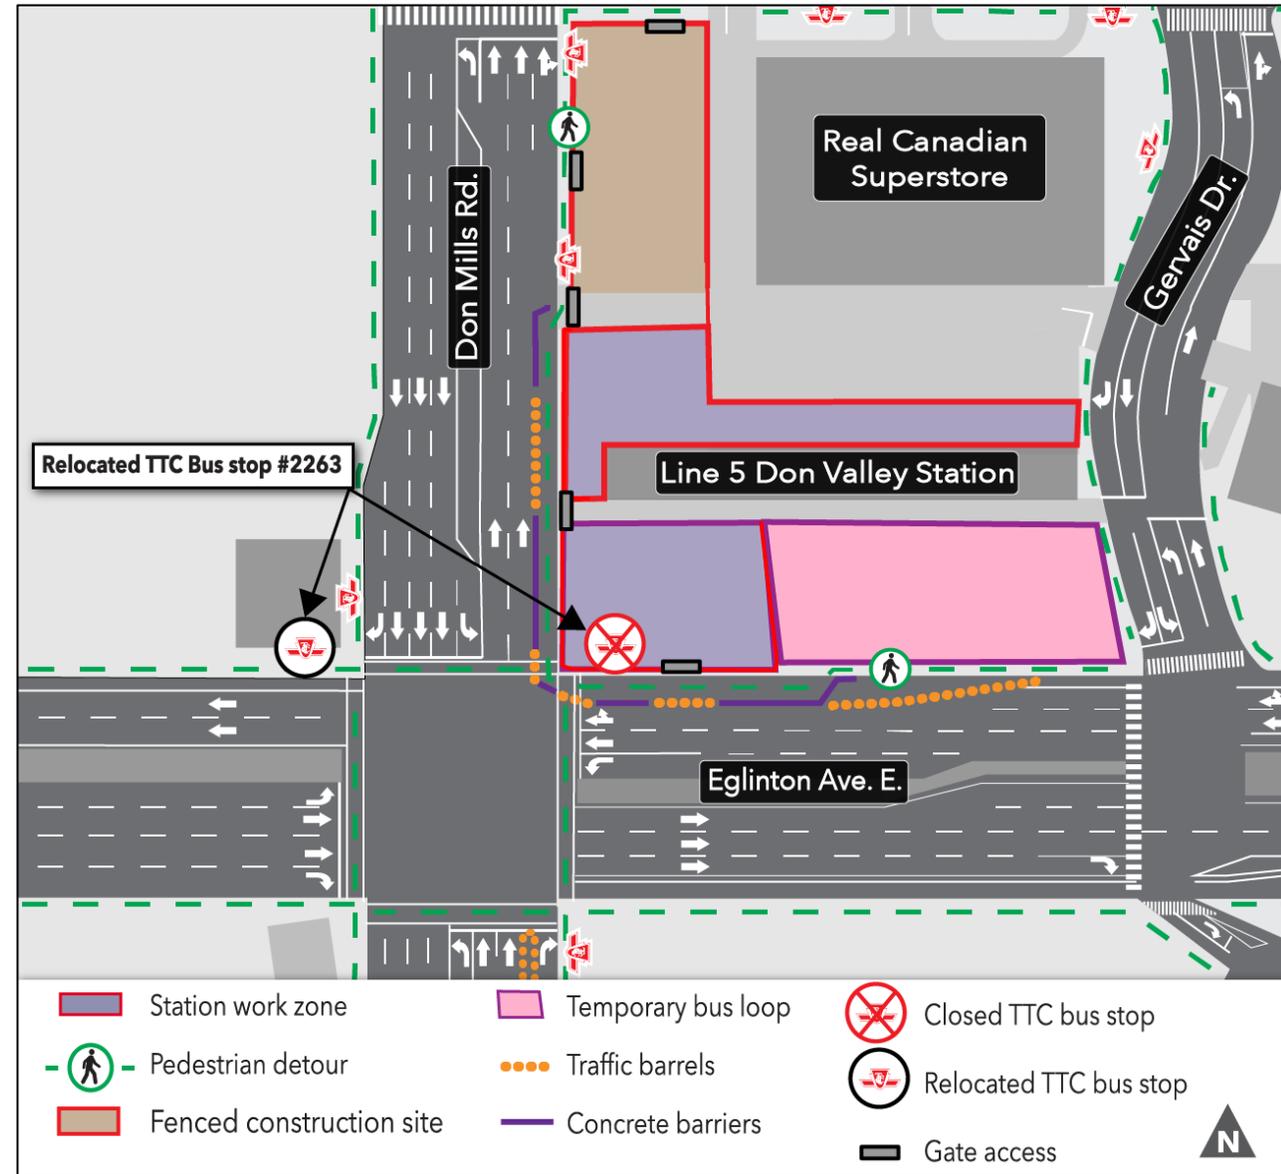

Construction Progress Photos: Don Mills Watermain Relocation



Don Mills Road and Wynford Drive - Oct. 1, 2025



Don Mills Road and Rochefort Drive - Oct 1, 2025

Construction Progress Photos: Pile Drilling at Don Valley Station



Drilling and ground clearing at D-40 - Oct 1, 2025



Spoil bank - Oct 1, 2025



Support Drilling at D-40 - Oct 1, 2025

Construction Progress Photos: Don Valley Station



North end of the guideway - Oct. 1, 2025



Don Valley Station construction site - Oct. 1, 2025

Construction Update: Flemingdon Park Station


EIGHT WEEK LOOK-AHEAD: October 8 - December 3, 2025

Start date and work hours	Work phase	Traffic and Pedestrian Impacts
As early as October 20	Site Preparation <ul style="list-style-type: none"> • Tree protection and tree removal • Installation of gates and fencing • Mobilization of equipment and material deliveries • Streetlight removals 	<ul style="list-style-type: none"> • Minor traffic and pedestrian detours on Don Mills Road and Eglinton Avenue for streetlight removals
Late November 2025	Hoarding installation <ul style="list-style-type: none"> • Installing plywood hoarding around the site 	<ul style="list-style-type: none"> • No traffic impacts are expected
December 2025	Site preparation continues <ul style="list-style-type: none"> • Set-up of offices and parking • Stockpiling materials and delineating work areas • Installation of light poles, generators, and transformers 	<ul style="list-style-type: none"> • Temporary traffic lane reductions and sidewalk closures on the west side of Don Mills Road • Exact traffic, pedestrian, and transit impacts to be determined. Details to be communicated at future CLC meeting.

- *Site preparation activities will take place within and around the Flemington Park Station site.*
- *Expected work hours are Monday to Friday between 7 a.m. - 5 p.m.*

Flemingdon Park Station: Site Staging and Traffic Maps

Starting as early as October 20, 2025

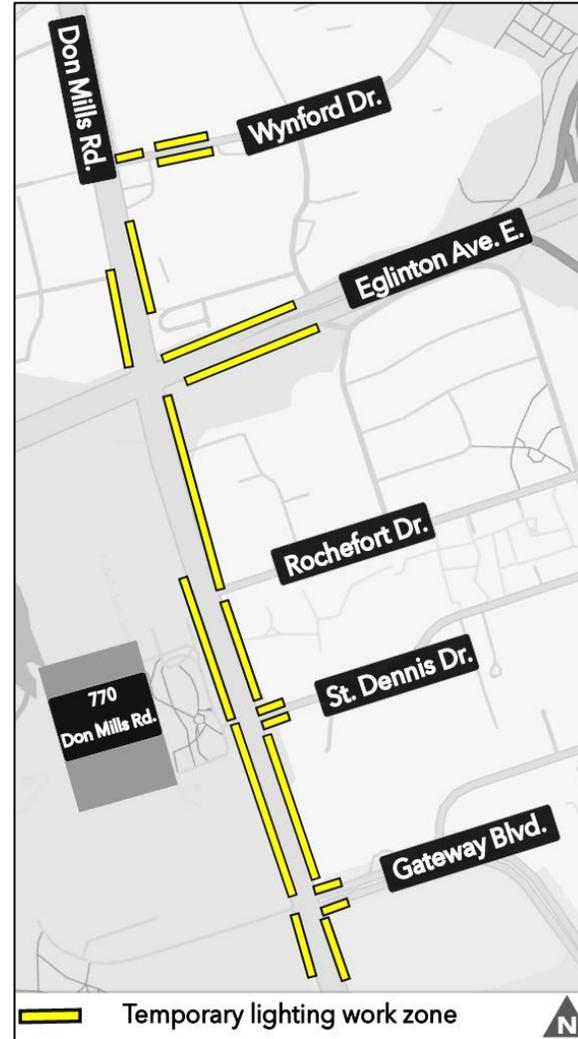

Construction Progress Photos: Flemingdon Park Station



Ongoing and Upcoming Traffic Impacts

Don Mills Rd. Watermain Relocation Traffic Impacts - 2025

Date	Type of Work	Traffic Impacts	Pedestrian Impacts
As early as October 14, 2025 One (1) week	<ul style="list-style-type: none"> Phase 12 - Watermain tie-in to the existing system. Testing and commission of new water distribution system. On the west side of Don Mills Road northbound, just north of Eglinton Ave East in front of bus terminal. 	<ul style="list-style-type: none"> Will maintain a minimum of two lanes of traffic north bound and south bound on Don Mills Rd. No left turns on Don Mills Rd. Southbound on to Eglinton Ave. E. eastbound 	<ul style="list-style-type: none"> N/A.
As early as October 21, 2025 Four (4) weeks	<ul style="list-style-type: none"> Phase 13 - Watermain installation of 300 mm pipe on the west side of Don Mills Rd., south of Eglinton Ave East. 	<ul style="list-style-type: none"> Vehicular traffic will shift to the east side of Don Mills Rd. between Eglinton Ave East and St. Dennis Dr. 	<ul style="list-style-type: none"> N/A.

Station and Guideway Traffic Impacts - Fall 2025 to Summer 2030

Date	Type of Work	Traffic Impacts	Pedestrian Impacts	Transit Impacts
As early as October 14, 2025 for five dates	<ul style="list-style-type: none"> Trenching to establish a water connection for the slurry plant 	<ul style="list-style-type: none"> Short-term lane reduction on Wynford Dr. to one lane of traffic in both directions at night - 9:00 p.m. to 5:00 pm Full road closure on Wynford Dr. at night between 1:30 a.m. to 5:00 a.m. 	<ul style="list-style-type: none"> Short-term sidewalk closures on north and south side of Wynford Dr., east of Don Mills Rd. 	<ul style="list-style-type: none"> N/A
Early November 2025 to late April 2029	<ul style="list-style-type: none"> Don Valley Station construction Site preparation activities 	<ul style="list-style-type: none"> Closure of the westbound right lane on Eglinton Ave East between Don Mills Rd. and Gervais Dr. Lane closure of the northbound right lane Don Mills Rd., between Eglinton Ave East and Wynford Dr. 	<ul style="list-style-type: none"> Bike lane closure will require cyclists to dismount and use temporary pedestrian walk Sidewalk will be moved into closed traffic lanes to ensure pedestrian safety and maintain connectivity 	<ul style="list-style-type: none"> Bus stop #2263 on Eglinton Ave East will be moved to north-west corner of Don Mills Rd. and Eglinton Ave. E. Bus stop #9125 on Don Mills Rd. will be moved
Late December 2025 to June 2029	<ul style="list-style-type: none"> Flemingdon Park Station construction Guideway piling 	<ul style="list-style-type: none"> Temporary lane reduction to southbound and northbound through lanes on Don Mills Rd. between Eglinton Ave East, Rochefort Dr., St. Dennis Dr. and Gateway Blvd. Two lanes of traffic to be maintained in both directions 	<ul style="list-style-type: none"> Sidewalk closure on the west side along Don Mills Rd. between Eglinton Ave East and Gateway Blvd. Sidewalk will be moved into closed traffic lanes to ensure pedestrian safety and maintain connectivity between St. Dennis Dr. and Gateway Blvd. 	<ul style="list-style-type: none"> Bus stop #15731 to be moved further north Bus stop #1935 will be relocated to the southwest corner of Don Mills Rd. and Gateway Blvd. Southbound bus stops will remain open on temporary platforms

Construction lookahead schedules

2025 Construction look-ahead

Timing	Activity	Location	Details and Purpose
Fall	<ul style="list-style-type: none"> Bus loop construction completion 	<ul style="list-style-type: none"> Eglinton Ave. E. and Gervais Dr. 	<ul style="list-style-type: none"> Temporary loop for Eglinton Crosstown bus while Don Valley Station is under construction.
	<ul style="list-style-type: none"> Watermain relocation phase 12 Watermain relocation phase 13 	<ul style="list-style-type: none"> Don Mills Rd., north of Eglinton Ave. E. Don Mills Rd., south of Eglinton Ave. E. 	<ul style="list-style-type: none"> Test and commission new 750 mm watermain system. Install, test and commission 300 mm watermain system.
	<ul style="list-style-type: none"> Piling and pier construction for tail track segment 	<ul style="list-style-type: none"> Don Mills Rd., north of Eglinton Ave. E. 	<ul style="list-style-type: none"> Foundation and pier construction starts north of Don Valley Station
	<ul style="list-style-type: none"> Don Valley Station site preparation 	<ul style="list-style-type: none"> Don Mills Rd. and Eglinton Ave. E. 	<ul style="list-style-type: none"> Stone sculpture removal and storage, installation of hoarding,
	<ul style="list-style-type: none"> Piling and pier construction for Don Valley Station 	<ul style="list-style-type: none"> Don Mills Rd. and Eglinton Ave. E. 	<ul style="list-style-type: none"> Fencing, signage, gates, temporary facilities, vegetation/tree removal, etc.
	<ul style="list-style-type: none"> Hydro Duct Bank installation Site preparation 	<ul style="list-style-type: none"> 770 Don Mills Road 	<ul style="list-style-type: none"> Preparatory work for Hydro Duct Bank installation Prepare the property at 770 Don Mills Rd for construction of the elevated guideway and Flemington Park Station.
Winter	<ul style="list-style-type: none"> Don Valley Station site mobilization for piling 	<ul style="list-style-type: none"> Don Mills Rd. and Eglinton Ave. E. 	<ul style="list-style-type: none"> Site preparation Start secant piling for station basement and excavation.
	<ul style="list-style-type: none"> Installation of guideway wall for secant piling Piling and pier construction for guideway 	<ul style="list-style-type: none"> Don Valley Station to Flemington Park Station 	<ul style="list-style-type: none"> Installation of fencing and signage, hoarding and grading

Discussion

Action Log

#	Questions Asked / Action Item	Response/Resolution	Due Date / Status
1			

Appendix
